



Spring 2026 Facilities Bond Program Update

Construction Network
El Segundo, CA

Alix Walsh O'Brien, FAIA
Deputy Chief Facilities Executive

May 21, 2026



LAUSD
UNIFIED

Capital Bond Program



How We Deliver The Work

A Large Capital Program, Deliberately Improving Execution


- One of the largest public-sector capital programs in California
- Focused effort over the last two years to improve planning and delivery
- Clear expectations around accountability, performance, and predictability
- Continuous improvement as a core operating principle



Projects Underway

889 Active Projects Valued at ~ \$9.5 Billion

In Pre-Construction
688 Projects
\$4.7 Billion

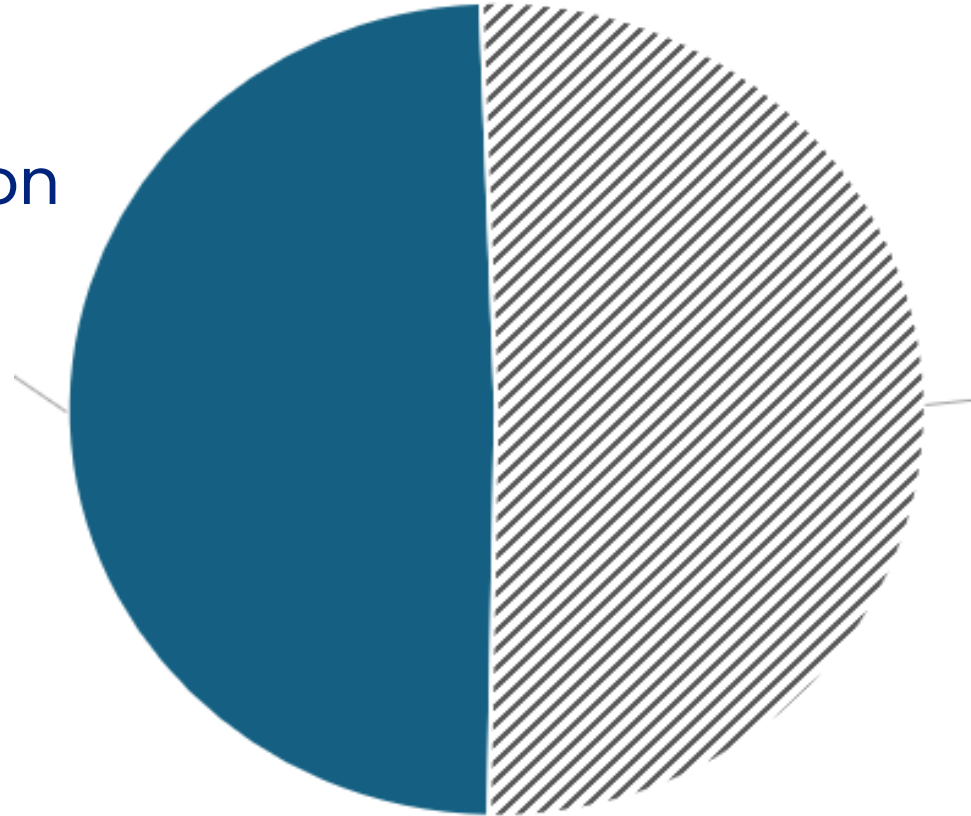

Under Construction
201 Projects
\$4.8 Billion

One-Year Look-Ahead > \$1 Billion

Programs include:

Project Type	No. of Projects *	Project Budget	Anticipated Bid Advertisement*
Classroom Upgrade Projects	47	\$406 million (\$5M-\$12M per project)	Q3 2026 – Q1 2027
Critical Replacements/Upgrades	30	\$226 million (hvac, roofing, etc.)	Q2 2026 – Q2 2027
Green Schoolyard Upgrade Projects	14	\$90 million (\$5M-\$7M per project)	Q3 2026 – Q2 2027
Barrier Removal (ADA) Projects	14	\$86 million (\$1M-\$12M per project)	Q2 2026 – Q2 2027
Playground & Campus Ext Upgrades	8	\$88 million (\$9M-\$11M per project)	Q1 2027 – Q2 2027
EEC Outdoor Classrooms	10	\$57 million (\$1M-\$8M per project)	Q3 2026 – Q2 2027
Athletic Improvement Projects	7	\$52 million (\$1M-\$14M per project)	Q2 2026 – Q2 2027
Wellness Clinic Projects	2	\$49 million (\$24M-\$25M per project)	Q2 2026
Seismic Retrofits	3	\$23 million (\$6M-\$8M per project)	Q1 2027 – Q2 2027
Outdoor Learning Environment	7	\$18 million (\$2M-\$3M per project)	Q2 2026 – Q3 2026

*Approximate and subject to change

Key 2027 Procurements

Design-Bid-Build Projects

- **Green Schoolyard Upgrade & Improvement Projects**
11 projects (\$71M) – campus-wide landscape, shade, outdoor classrooms, accessibility
- **Playground and Campus Exterior Upgrade Projects**
8 projects (\$90M) – campus-wide hardscape, landscape, shade, exterior paint, play elements, and ADA accessibility
- **Athletic Improvement Projects**
7 projects (\$54M) – upgrades to high school competitive athletic facilities
- **Roofing, HVAC Upgrades, Barrier Removal (ADA) Projects, and more**

Design-Build Projects

- **Seismic Upgrade Projects**
3 projects (\$23M) – removal and replacement of structurally deficient buildings



LAUSD
UNIFIED

Palisades Recovery Projects



Palisades Charter High School

Phase 1 – Interim Housing, Repairs and Remediation – Completed

Phase 2 – Permanent Reconstruction – Anticipated Completion 2029

New Classroom Building

- 21 General classrooms
- 6 Specialty classrooms
- Administration spaces

Palisades Academy

- 3 General classrooms
- Faculty/Staff offices


Athletic Field Areas

- Ancillary Field Buildings
- Baseball Field
- Other related amenities

Electrical Service Upgrades

Project Budget: \$266 million

Bid Advertisement: May 2026

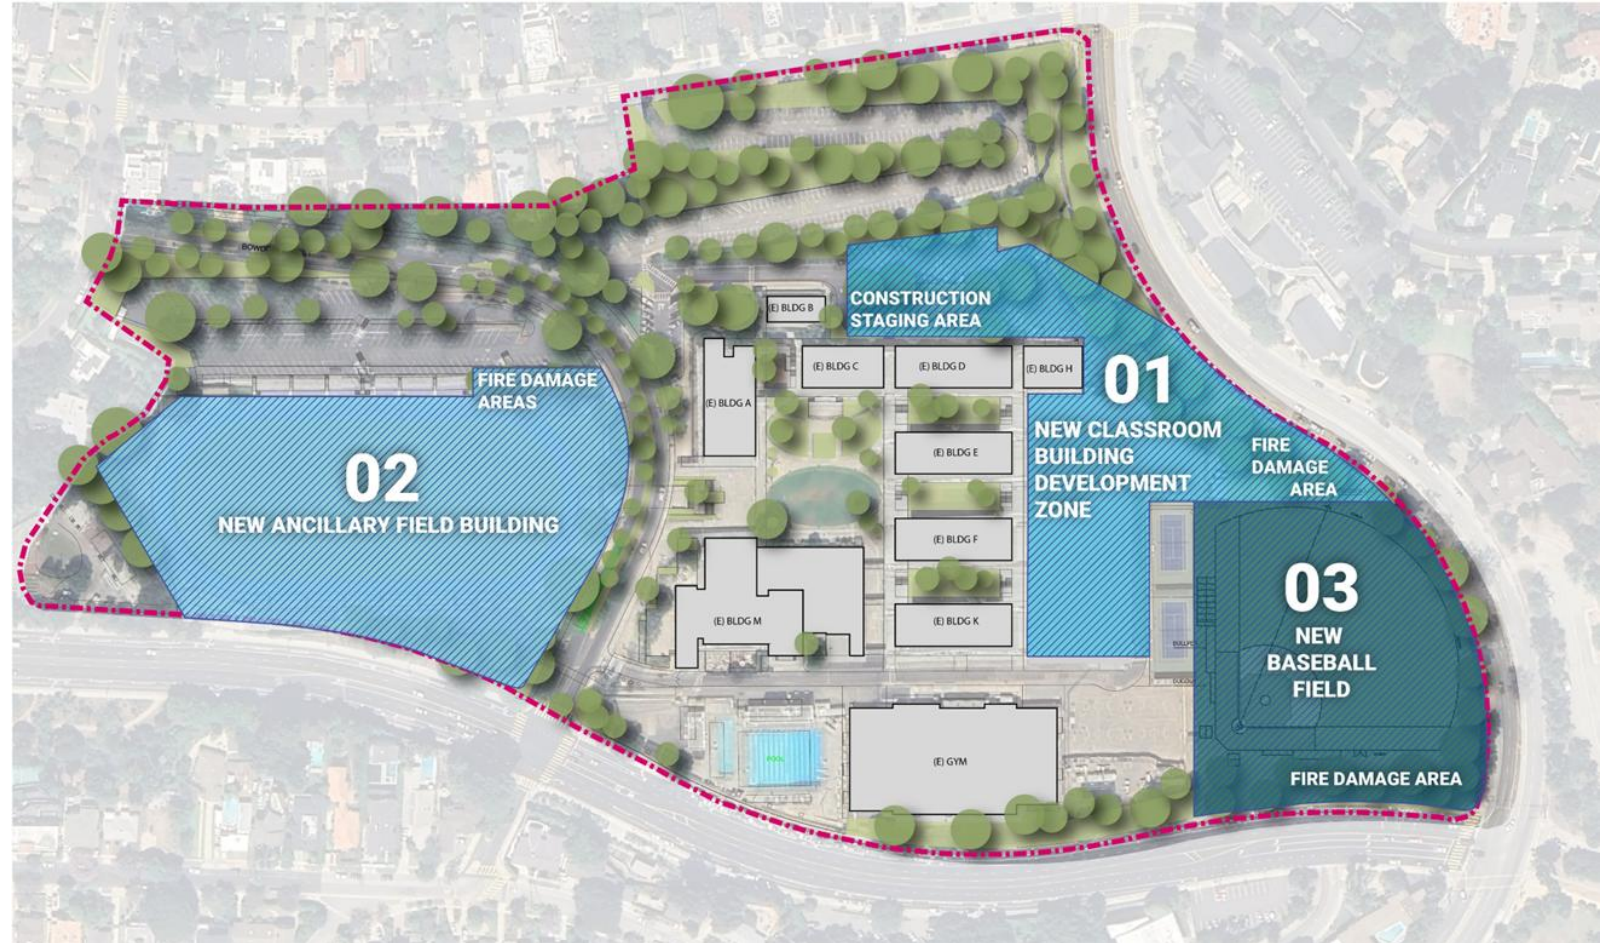

Palisades Charter High School Campus Reconstruction Renderings



Marquez Charter Elementary School

Phase 1 – Interim Housing, Repairs and Remediation – Completed

Phase 2 – Permanent Reconstruction – Anticipated Completion 2028

New Classrooms

- 13 General classrooms
- 4 Kinder/TK classrooms
- Flexible learning/maker spaces
- Parent center

Library

Administration

Food Services

Multi-Purpose Room

Electrical Service Upgrades

Project Budget: \$202 million

Bid Advertisement: April 20, 2026 Release



Marquez Charter Elementary School Campus Reconstruction Renderings



Palisades Charter Elementary School Campus Reconstruction

Repair and Upgrades to Existing Buildings

Exteriors – Paint and new marquee signage.

HVAC – Full replacement including rooftop units and distribution ductwork.

Administrative Area – Layout modifications for improved visual connection and functional flow. New furnishings and finishes.


Interior Finishes – Upgrades of finishes, including paint, ceilings, window treatments, flooring, and new furnishings.

Restrooms – Accessibility Upgrades to existing Restroom facilities to meet current regulatory requirements.

Food Services Building – Upgrades of finishes and equipment.

Project Budget: \$135 million

Bid Advertisement: March 23, 2026 Release

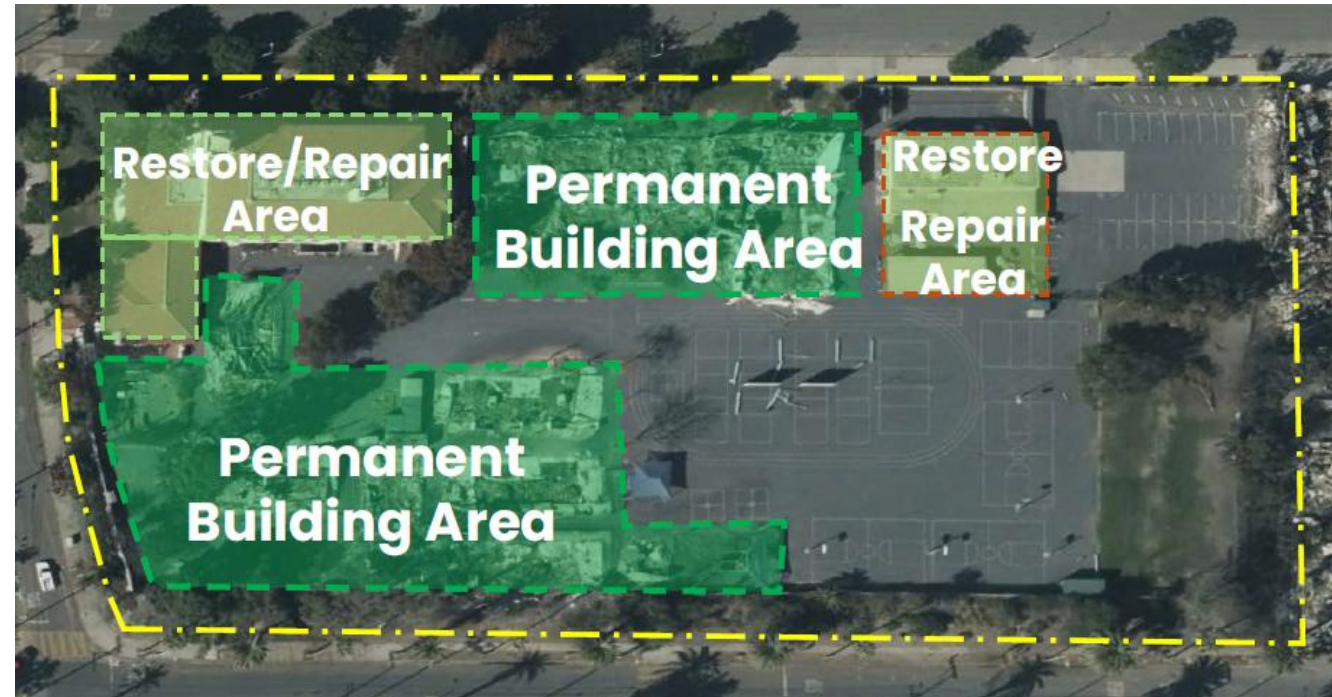

Palisades Charter Elementary School Permanent Reconstruction

New Classrooms (14 CSRs)

- 7 General Classrooms
- 5 Kinder/TK Classrooms
- Flexible Learning/Maker Space Classrooms
- Resource Specialist Rooms

Multi-Purpose Room

Outdoor Areas

- Lunch Shelter
- Outdoor Play Areas / Learning Environments

Electrical Service Upgrades



Palisades Charter Elementary School Campus Reconstruction Renderings



Practice

Project Delivery Improvements

Business Practice Improvements

- **Updated Specifications Implemented**
 - Updated Mechanical, Electrical, Plumbing and EMS Sections
 - Balance of Specifications under final review
 - Updating Information Technology (Classroom Technology)
- **Increased Due Diligence to Minimize Change Order Processing and Schedule Impacts**
 - Expanded checklists developed to minimize unforeseen conditions
- **Increased General Contractor Markup from 5% to 10%**
- **Increased Pool of Estimating Consultants**
- **Contractor Engagement**

Expanding Procurement and Delivery Options

Increased Use of Design-Build and Alternative Design-Build

- Reduces delivery time frames for procurement, design and construction
- Integrates contractor expertise early in design to improve phasing, constructability and logistics planning
- Utilizes best-value selection criteria with emphasis on qualifications, experience, and cost factors
- Ongoing cost alignment and informed decision-making throughout design
- Reduces project risk and minimizes change orders through early coordination

Ongoing Focus Areas

- Consistent early site analysis including pot-holing and destructive testing
- Industry Standard approach to project specifications
- Alignment of delivery method to project type and complexity
- Expanded contractor outreach and prequalification efforts
- Improved fair cost estimating and escalation process
- Reduce Change Order backlog
- Reduce time frame for design professional contracting process
- Increase training across departments
 - Risk Management training focus on effective change management
 - Annual CMAA training provided

AI and Innovation in Project Delivery

- Learning about emerging trends and applications of AI tools from Architects and Contractors
- Saving time and improving quality of both design and construction
 - Clash detection
- Insights from these discussions may inform:
 - Future procurement and contract strategies
 - Internal operational improvements
 - Enhanced project coordination and delivery efficiency



Changes in Educational Planning

Greening Investments

Outdoor Learning Environments

- Construction of approx. 2,000 sq. ft. outdoor classroom
- Landscape (trees and pavers)
- Shaded seating areas
- Internet access and electrical outlets
- ADA accessibility improvements

Green Schoolyard Upgrades

- Replace asphalt with green/natural elements such as outdoor learning spaces, landscaping & trees, grass playfields
- ADA accessibility improvements
- Removal of underutilized portable buildings
- Utility infrastructure improvements as necessary



48 Classroom Upgrade Projects

Approximately 50 classrooms per site

Schools will remain operational

- Swing space may be utilized
- Swing shifts may be required

Work may include:

- New interactive mobile display boards
- Replacement of damaged whiteboards
- Sound enhancements – Teacher oration
- New classroom furniture
- Replacement of damaged window blinds
- Interior painting
- Address damaged ceiling tiles
- Security door locks
- Limited electrical upgrades to support new classroom technology

Pacoima MS



Dodson MS



Wellness Center Projects

Comprehensive Health Care:

- Physical Health
- Mental Health
- Dental Health
- Health Education and Career Pathways

Scope Includes:

- New ~6,000SF wellness center building
- Site improvements (parking lot, fencing/gates, landscape, hardscape, and infrastructure upgrades)
- Code and accessibility compliance





LAUSD
UNIFIED

Transformation

- Capturing underutilized space for new uses
- Replacing relocatable classrooms with right-sized new buildings
- Transforming existing classroom space into future ready learning environments

Kenter Canyon Elementary School Courtyards





**Calabash Elementary School
Classroom Replacement**



**Shenandoah Elementary School
Comprehensive Modernization**





Dena ES



2nd St. ES



Dena ES



2nd St. ES



Malabar ES



Mayall ES



Harbor City ES

SEEDS Learning Gardens



Carthay STEM Magnet

Hollywood High School

Conversion of a former Auto Shop to an Arts, Media and Entertainment Center



Before



After



After



After



After



Before



After

Sylmar High School Conversion of a Metal Shop into a Medical Simulation Lab

Opportunities for Emotional Connections

Unspoken Messages

- Providing for communal activities
- Reinforcing the excitement of movement & energy
- Balancing the stimulation of passage with the opportunity to stop & rest
- Emphasizing the unique attributes of place & community





Palisades Charter High School
DLR



LAUSD
UNIFIED

Questions

 @LAUSD_Facilities
